

NAME	KANAK PANDEY
SRN	PES1UG24CS212
SECTION	D

EPICS -

Spaces / waste management

WM board

Summary

Timeline

Active sprints

Backlog

Calendar

List

Forms

Development

Docs

Reports

Search timeline

KP

Filter

Quick filters

	> Work	Status	Assignee		October
	Sprints			WM... WM... WM Sprin	
	Releases				
	WM-1 Route generation and optimization		Unassign...		
	WM-6 As a dispatcher, I want daily routes to i...	Done	Unassign...		
	WM-7 As a dispatcher, I want to manually tag ...	Done	Unassign...		
	WM-8 As a dispatcher, I want routes recalcula...	Done	Unassign...		
	WM-9 As a developer, I want a load test for ro...	Done	Unassign...		
	WM-2 Driver navigation		Unassign...		
	WM-10 As a driver, I want my assigned route t...	Done	Unassign...		

Jira

Search

+ Create

See plans

For you

Recent

Starred

Apps

Plans

Spaces

Spaces / waste management

WM board

Summary Timeline Active sprints Backlog Calendar List Forms Development Docs Reports

Search timeline

Filter

Quick filters

Work	Status	Assignee	October
Sprints			WM... WM... WM Sprint
Releases			
WM-2 Driver navigation		Unassign...	
WM-10 As a driver, I want my assigned route t...	Done	Unassign...	
WM-11 As a driver, I want GPS navigation to e...	Done	Unassign...	
WM-12 As a dispatcher, I want bin coordinate...	Done	Unassign...	
WM-3 Bin collection and status trac...		Unassign...	
WM-13 As a driver, I want a "Mark Collected" ...	Done	Unassign...	
WM-14 As a driver, I want a "Mark Missed" bu...	Done	Unassign...	
WM-15 As a supervisor, I want status updates ...	Done	Unassign...	

Today Weeks Months Quarters

Jira

Search

+ Create

See plans

For you

Recent

Starred

Apps

Plans

Spaces

Spaces / waste management

WM board

Summary Timeline Active sprints Backlog Calendar List Forms Development Docs Reports

Search timeline

Filter

Quick filters

Work	Status	Assignee	October
Sprints			WM... WM...
Releases			
WM-16 As a dispatcher, I want bin coordinates validated so that drivers are never...	Done	Unassign...	
WM-3 Bin collection and status tracking		Unassign...	
WM-13 As a driver, I want a "Mark Collected" button so that I can record each bi...	Done	Unassign...	
WM-14 As a driver, I want a "Mark Missed" button so that I can record bins I coul...	Done	Unassign...	
WM-15 As a supervisor, I want status updates validated so that the data I rely on i...	Done	Unassign...	
WM-16 As a driver, I want status changes to appear in the interface within 2 seco...	Done	Unassign...	
WM-17 As a driver, I want to acknowledge a confirmation and move to the next bi...	Done	Unassign...	
WM-4 Missed Pickup Handling and Reassignment		Unassign...	


Jira interface showing the "WM board" (waste management) in the "Timeline" view. The board displays a list of tasks under the "Work" section, categorized by "Sprints" and "Releases". The tasks are listed with their IDs, descriptions, status, and assignee.

ID	Description	Status	Assignee
WM-16	As a driver, I want status changes to appear in the interface within 2 seco...	Done	Unassign...
WM-17	As a driver, I want to acknowledge a confirmation and move to the next bl...	Done	Unassign...
WM-4	Missed Pickup Handling and Reassignment		Unassign...
WM-18	As a driver, I want to choose a reason when marking a bin missed so that ...	Done	Unassign...
WM-19	As a sanitation supervisor, I want a real-time alert when a bin is missed so...	Done	Unassign...
WM-20	As a dispatcher, I want missed bins automatically reassigned to a nearby ...	Done	Unassign...
WM-21	As a driver, I want to receive an updated route when a bin is reassigned to...	Done	Unassign...

Jira interface showing the "WM board" (waste management) in the "Timeline" view. The board displays a list of tasks under the "Work" section, categorized by "Sprints" and "Releases". The tasks are listed with their IDs, descriptions, status, and assignee.

ID	Description	Status	Assignee
WM-19	As a sanitation supervisor, I want a real-time alert when a bin is missed so...	Done	Unassign...
WM-20	As a dispatcher, I want missed bins automatically reassigned to a nearby ...	Done	Unassign...
WM-21	As a driver, I want to receive an updated route when a bin is reassigned to...	Done	Unassign...
WM-5	Compliance reporting		Unassign...
WM-22	As a supervisor, I want a daily emailed report of the percentage of sched...	Done	Unassign...
WM-23	As a supervisor, I want missed-pickup reasons included in the daily repor...	Done	Unassign...
WM-24	As a driver, I want to log a safety incident in the app so that it appears in ...	Done	Unassign...
WM-25	As a supervisor, I want safety incidents included in the daily report so tha...	Done	Unassign...

SPRINT 1

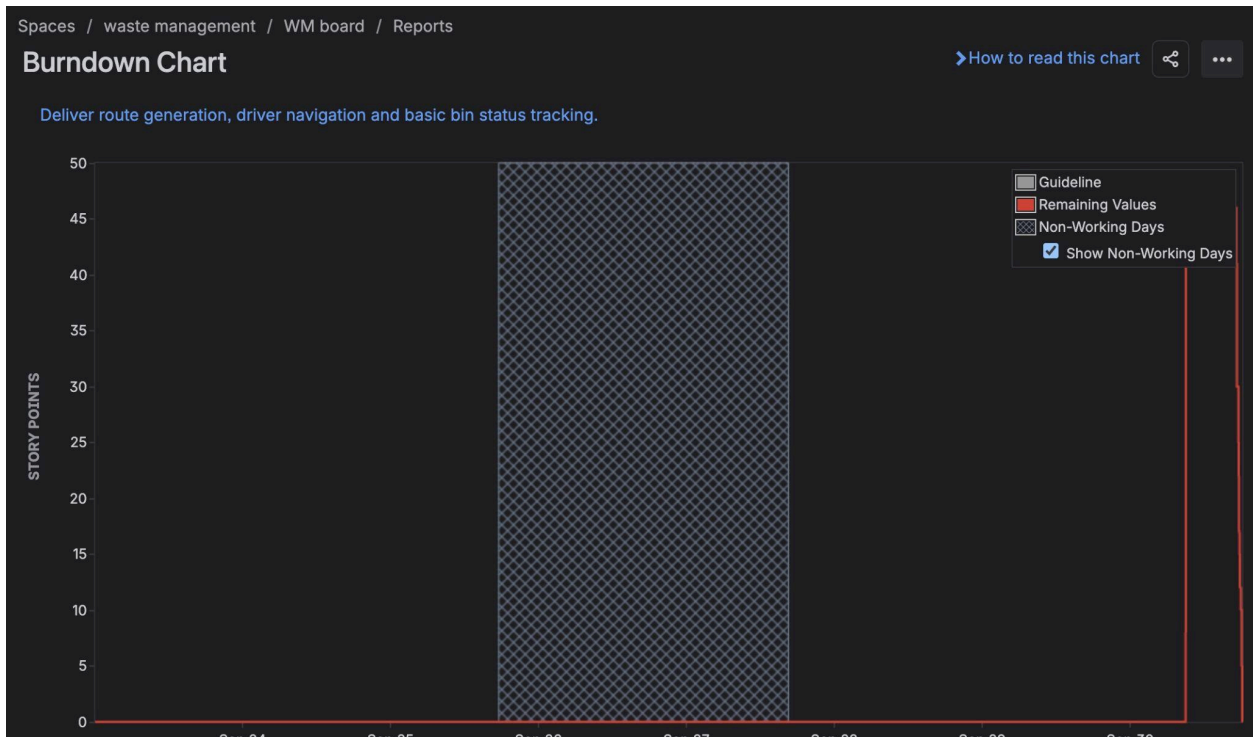

Sprint 1 (Sep 24 to Sep 30)

The sprint goal was "Deliver route generation, driver navigation and basic bin status tracking." The chart looks unusual. The remaining-work line stays at 0 from Sep 24 until Sep 30, then jumps to about 46 story points and drops back to 0 within a short time. This happened because the sprint's start date was earlier than the date the stories were actually added, so Jira recorded the sprint as empty until Sep 30. Jira treats stories added after a sprint starts as added scope, so the line rose instead of starting high and burning down. The steep drop that follows is the stories being moved from To Do to In Progress to Done within one session. No grey guideline is visible because the sprint started with 0 points, so the guideline sits flat at 0 under the red line. The chart is therefore an accurate record of what happened, but it doesn't show gradual progress, and it shows why all stories should be committed before a sprint is started.

SPRINT 2



Sprint 2 (Oct 1 to Oct 7)

The chart starts at about 32 story points, and the grey guideline slopes down to 0 by Oct 7, flat across the weekend (Oct 3 to 4) because those are non-working days. The red line falls almost vertically at the very start of the sprint because all stories were completed within minutes of starting. This chart has the correct shape, since the work was committed before the sprint began, but it is far ahead of the guideline because the work was simulated.

Reflection answers

1. Did your estimations reflect the actual effort?

Not in a measurable way. Sprint 1 held about 46 points and Sprint 2 about 32, but both sprints finished almost immediately, so the charts can't show whether the estimates matched real effort. The work was simulated by moving cards between columns, not by building the features. In a real project, I would expect the 8-point stories (fast route recalculation and automatic reassignment) to be the most likely to be underestimated because of their technical uncertainty, and they would probably need to be split into smaller stories.

2. Was your backlog well-prioritized?

Largely yes. Route generation and navigation were placed in Sprint 1 because every other feature depends on them, and reassignment and reporting came later because they rely on status data. The requirements document marks almost everything as High, so I also used dependencies to decide the order. The Sprint 1 chart showed a planning weakness, though: the stories were added to the sprint after it had started, so the prioritized scope wasn't locked in at the beginning.

3. How did your simulated sprint align with your plan?

Both sprints were completed, and all planned stories reached Done. Sprint 2 matched the plan: its scope was set before the start and it finished inside the one-week window. Sprint 1 did not match the plan cleanly. Its chart shows 0 points for the first six days and then a sudden jump to about 46, which means the scope was added after the sprint's start date. The sprint was finished, but the chart doesn't reflect a planned sprint with committed scope. Both sprints also finished far ahead of the guideline, which would be unrealistic for a real team.

4. What insights did the burndown chart give about your team's capacity?

The charts suggest the team completed about 46 points in Sprint 1 and about 32 in Sprint 2, but this can't be treated as true capacity, because the work was simulated and completed almost instantly. In a real team, finishing this far ahead of the guideline would suggest that the team committed to too little or estimated the work too high. The Sprint 1 chart also shows how scope added mid-sprint distorts a burndown chart, making progress hard to read and forecasting unreliable. To measure real capacity, the team would need several sprints with scope committed before the start and work completed gradually across the week.
